


FCC Type Acceptance
MX800 TCXO

TEMP°C	(PPM)
--------	-------

60	-0.216
50	-0.029
40	-0.022
30	0.147
20	0.282
10	0.325
0	0.344
-10	0.362
-20	0.446
-30	0.522

Equipment	Cal Due
-----------	---------

HP 8920A	8/2/98
Fluke 75	2/17/99
Ratelco pwr supply	N/A

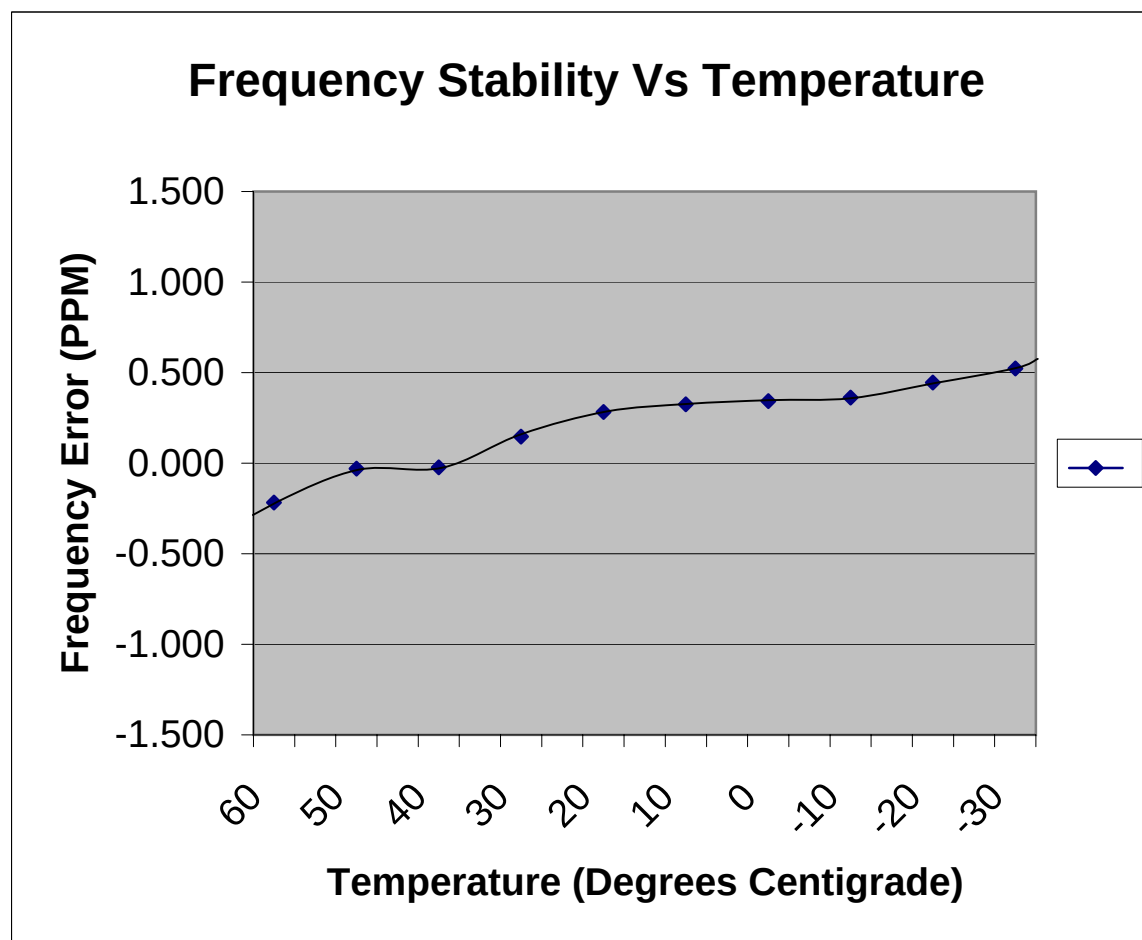

Test performed by:

Kenneth Klyberg
Engineering Technician
